

Climate Resilience Improvement Project – Component 2 & Additional Finance, Irrigation Department

Climate Resilience Improvement Project (CRIP) is executed by Ministry of Irrigation, Water Resources and Disaster Management with the financial assistance of the World Bank. The allocation for the Irrigation Department is Rs. 6,835 million to implement immediate flood and drought risk mitigation works of hydraulic infrastructure in downstream.

The project covers 11 Regions (Ampara, Anuradhapura, Batticaloa, Hambantota, Kurunegala, Monaragala, Polonnaruwa, Puttalam, Trincomalee, Kandy and Mannar) while giving benefits to 150,000 no of famer families for around 120,000 Ha of Irrigable Area.

The Cumulative Expenditure at the end of May 2019 is Rs. 4,902 million.


Table 1: Benefited Irrigation Schemes

Region	Scheme	No. of Farmer Families	Benefited area (Ha)
Ampara	Senanayake Samudraya	14,989	15,013.00
Anuradhapura	Padaviya	5,060	3,034.00
	Tissa wewa	434	200.00
	Nuwara wewa	433	1,210.00
	Hurulu wewa	1,050	200.00
Kurunegala	Hakwatuna oya	2,536	2,575.30
Batticaloa	Navakiri	550	7,085.02
	Unnichchai	1,076	5,164.78
	Vahanery	3,150	4,000.00
	Rugam	3,075	3,948.18
Monaragala	Muthukandiya	834	809.37
	Saddhatissa	375	170.37
	Horabokka	240	141.64
	Halmillapillewa	139	105.22
	Balaharuwa	392	169.56
	Dambewewa	270	131.52
	Debara Ara	72	87.01
	Kandiyapita & Hambegamuwa	561	403.87
	Monerawana	160	60.70
Puttalam	Inginimitiya	4,500	3,566.00
Polonnaruwa	PSS	12,130	10,194.00
	Girithale	6,000	3,035.00
	Minneriya	12,000	10,117.00

	Kaudulla	6,500	5,463.00
	Elahera	13,500	6,678.00
Trincomalee	Kantale	10,000	4,000.00
	Mutur	10,000	7,000.00
Hambantota	Muruthewela	2,083	4,426.00
	Yodhawewa	2,500	3,267.00
	Debarawewa	500	945.00
	Tissa wewa	1,200	2,750.00
	Ridiyagama	2,864	8,497.00
Mannar	Giants Tank	22,299	612.00
	Neelamadu, Vellalankattu, Chalampan	56	102.00
	Akathymurippu	2,600	1,626.00
Kandy	Minipe	6,824	3,239.00
Total		150,952	120,026.54

Table 2 : Current Progress of Contracts

Component 2		
Region	Total no of Contracts	Completed contracts up to August 2018
Ampara	15	14
Anuradhapura	36	34
Batticaloa	7	5
Kurunegala	22	21
Polonnaruwa	124	97
Puttalam	21	14
Trincomalee	51	43
Hambantota	55	43
Monaragala	15	10
	346	281
Additional Finance		
Region	Total no of Contracts	Completed contracts up to August 2018
Ampara	18	12
Anuradhapura	12	3
Batticaloa	1	
Hambantota	10	2
Mannar	5	2
Trincomalee	4	
Moneragala	7	
Kandy	8	3
Kurunegala	1	
Polonnaruwa	1	
	67	22

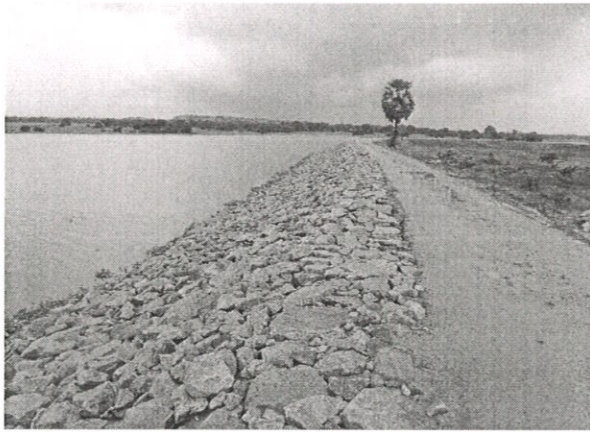

Impr.to Valathapitty Tank bund including Rip Rap in Ampara & Reconstruction of Nelluchchenai Anicut in Batticaloa



Canal D – 5, Hakwatuna Oya Scheme in Kurunegala & CRIP/WORKS/ID/PUT/CP/215-3 in Puttlam



CRIP/WORKS/ID/HAM/S/284 in Hambantota & Construction of Irrigation channel from Sadawakkai High Level channel to Sinaveli Sinnalamveli tract in Batticaloa
